



TOWN OF UXBRIDGE
MASSACHUSETTS
Department of Public Works

BENN S. SHERMAN, P.E.
Director of Public Works

147 Hecla Street
Uxbridge, MA 01569
(508) 278-8616
Fax (508) 278-3179

RT 122 WATER MAIN REPLACEMENT PROJECT CONTRACT NO. 11, DWSRF NO. 3879

PROJECT UPDATE #3 – May 9, 2016

UPCOMING WORK

The following work is proposed for this project for the week of May 14, 2016:

- Finishing water main from Fletcher St. to Hazel St.
- Chlorinate the section of water main from Blanchard Ave. to Fletcher St. and pressure test for reliability. Anticipate taking water samples on 5/10 & 5/11.
- Possibly start working on the new water main from Seagrave St. to Douglas St. starting 5/10 and work on the section for the remainder of the week.

PROJECT TEAM

Project Owner: **Town of Uxbridge**
Benn Sherman, P.E.
Director of Public Works
(508) 278-8616
bsherman@uxbridge-ma.gov

Contractor: **Ludlow Construction**
Michael Pio, Project Manager
Arthur Vilacha, Superintendent

Jim Boliver
Water Operations Supervisor
(508) 278-8631
jboliver@uxbridge-ma.gov

Project Office: **Otis Street Yard**

Engineer: **Tata & Howard**
Jon Gregory, Project Manager
Steve Defeo, Resident Project Representative

PROJECT STATUS

The project is approximately 35% completed. The following is a summary of the activities underway and/or completed to date.

1. Contractor mobilized back on site in early March 2016. They are utilizing a staging area off East Hartford Avenue next to CVS.
2. Contractor installed temporary bypass main in the area of the Hannaford's plaza and from Seagrave to the town center. Systems were disinfected and the residents and businesses were transferred to the temporary main.
3. Phase 2 of construction includes the bridge crossing, the remaining 700 feet in front of the Hannaford's plaza and remaining work from Seagrave to Country Squire Road.
4. Performed permanent paving along North Main Street.



5. Completed the bridge crossing over the Rivulet Brook.

Motorists can expect delays while traveling through the construction area and should seek alternate routes when possible. Funding for this project is through the State Revolving Fund (SRF) and the Water Pollution Abatement Trust.

PROJECT CHANGES

There are no changes to the contract.


Attachment: Phase 2 Locus Map

Rt. 122 Water Main Replacement Project

Phase 2 Project Locus

Legend

-  Phase 2a - Hanaford's
-  Phase 2a - Rivulet Bridge Crossing
-  Phase 2b - Seagrave to Common
-  Phase 2c - Common to Park Street
-  Phase 2d - Park Street to Country Squire

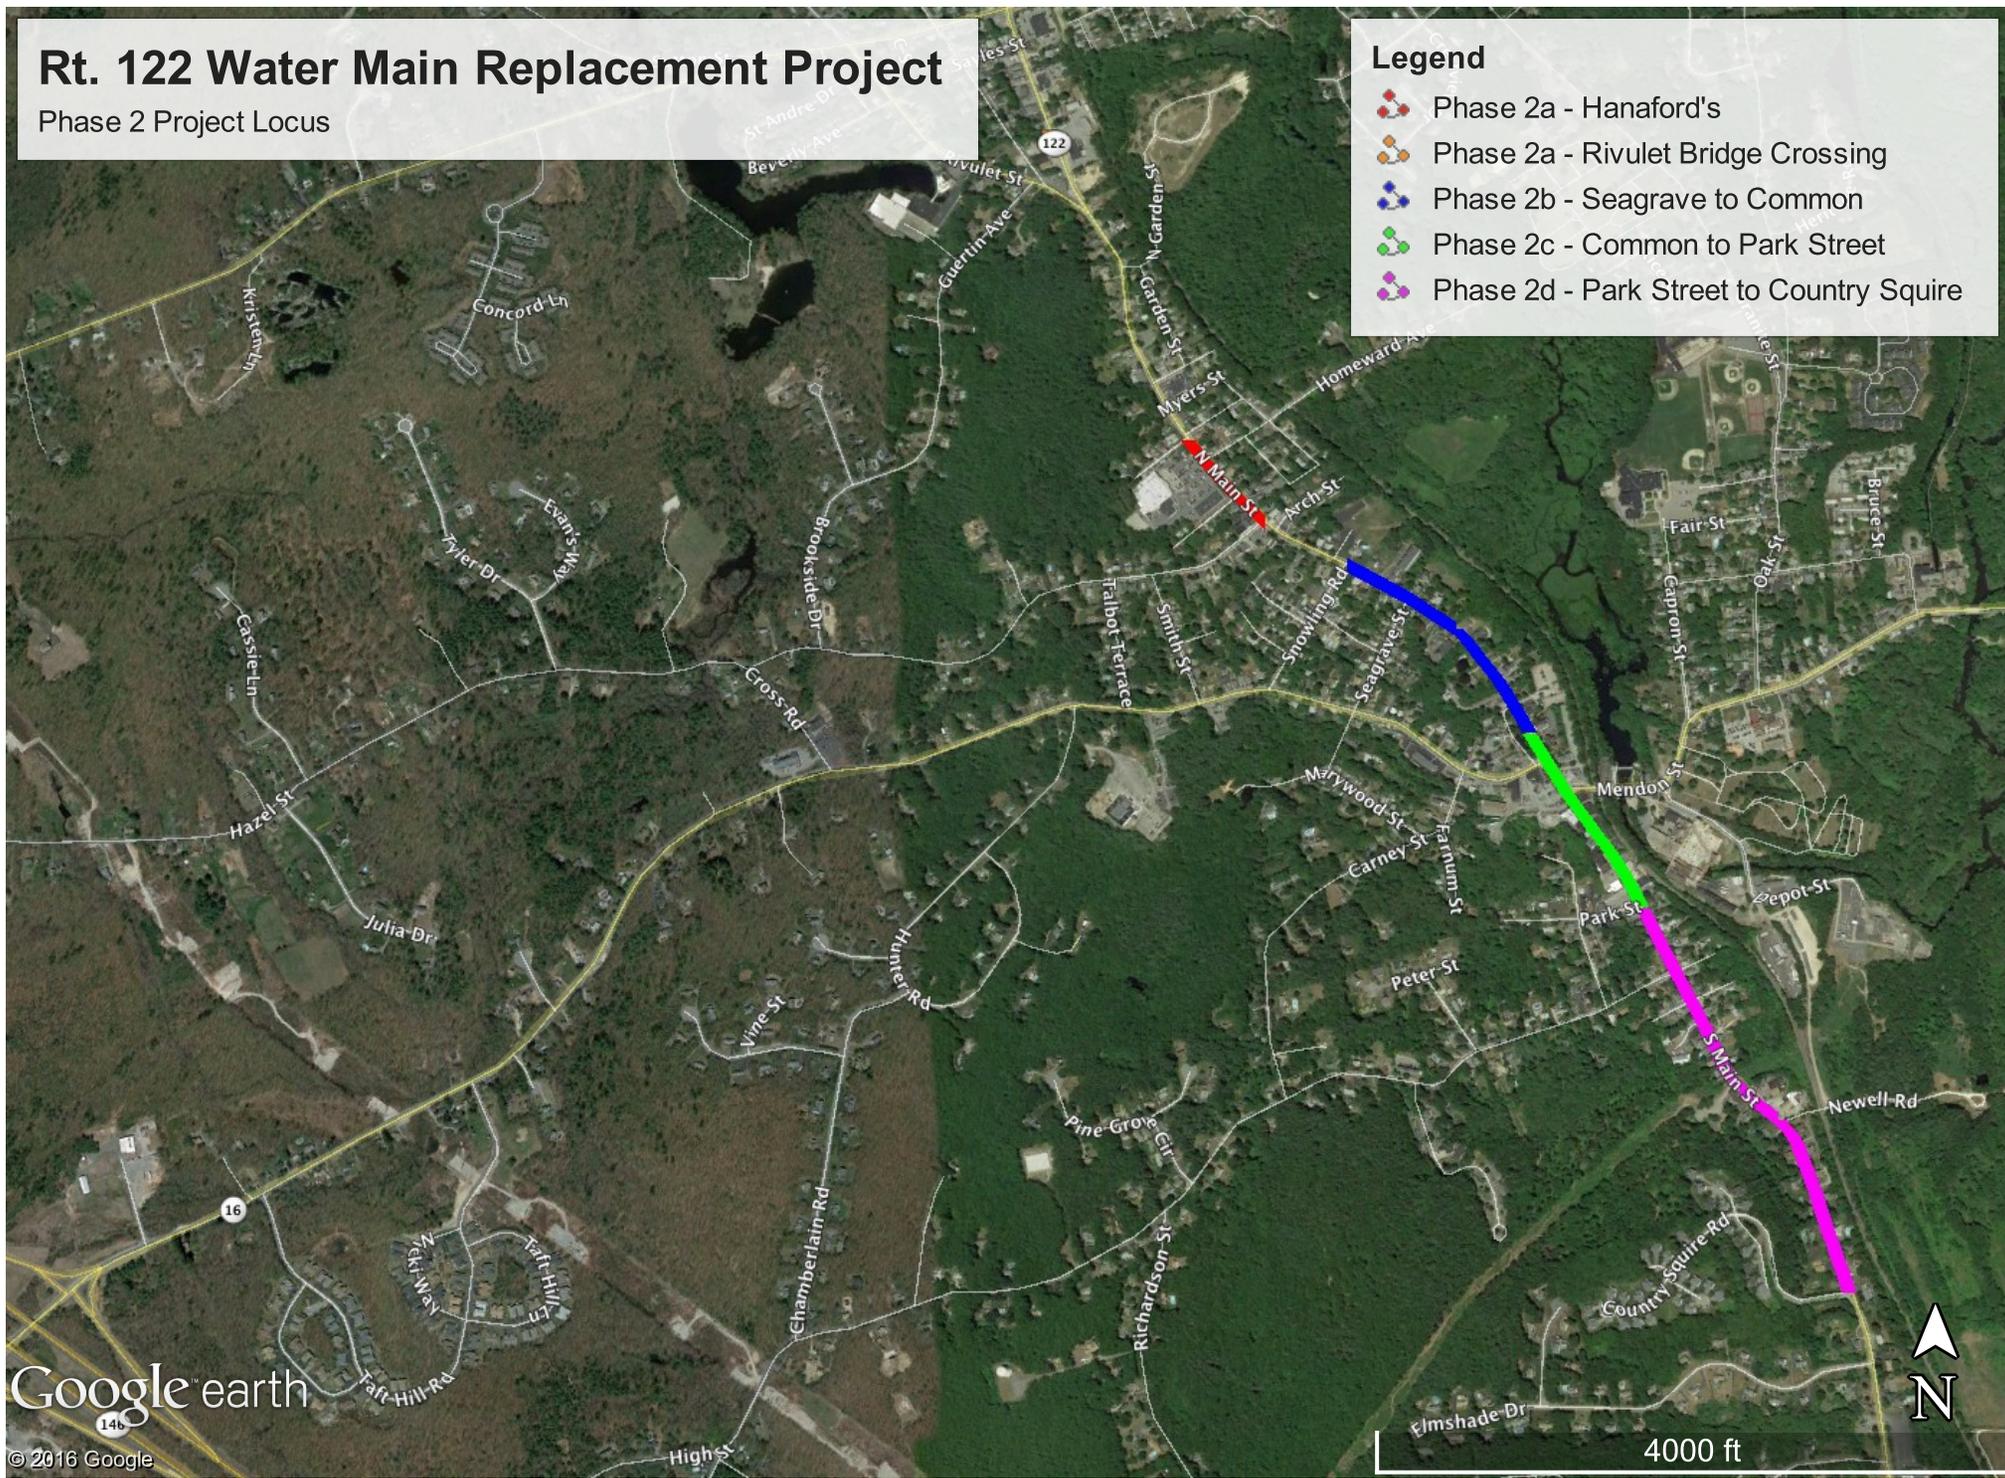

Google earth

© 2016 Google

4000 ft
